



Presentation to Board of Education

December 7, 2021



- 1. Community / Staff / Agency Interactions
- 2. Site Plan Overview
- 3. Building Floor Plans
- 4. Building Elevation
- 5. Phase 2 Design Development Approval Request
- 6. Next Steps
- 7. Questions & Answers





Community Interactions




- > Stakeholders Meeting (October 30, 2020)
- Staff Meeting (November 23, 2020)
- Public Meeting(December 1, 2020)
- Staff Programming
 (April May 2021 / November 2021)
- > Student Focus Group (April 13, 2021)
- > Parent Focus Group (April 22, 2021)
- City Agency Coordination Meetings Ongoing (April / May / June / July / August . . . 2021)
- Community Meetings / Presentations Ongoing
 (May 10, 2021 / July 14, 2021 / Sept. 7, 2021 / Oct. 5, 2021 / Nov. 16, 2021...)






Site Plan Overview



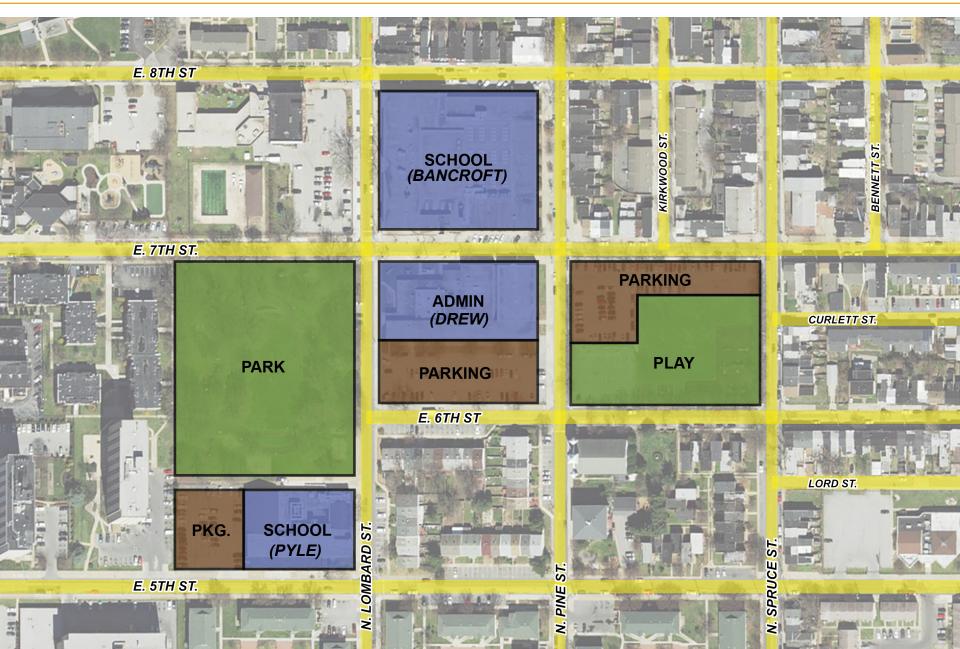



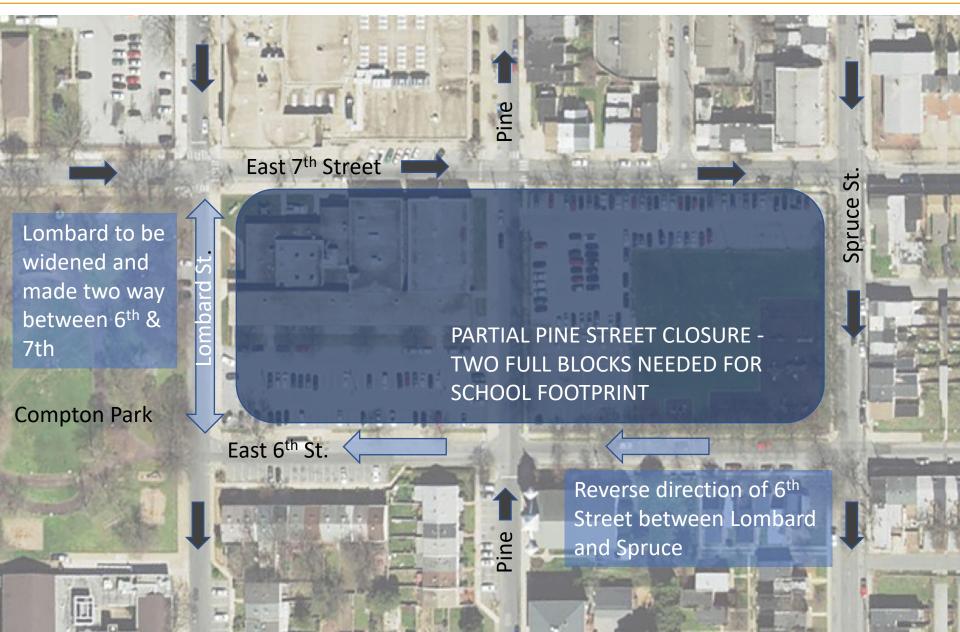













Building Floor Plans









Building Elevation








Phase 2 DD Approval



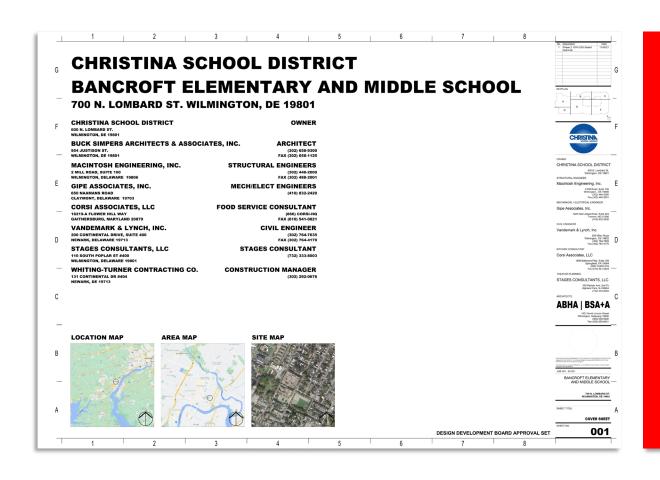

Request for Board
Approval

NEW PROJECT FUNDING ALLOCATION

FY 2021: \$7.5M

Allocated by State of Delaware Toward City of Wilmington projects Directed to Bancroft School project

FY 2022: \$65M

Allocated by State of Delaware Directed to Bancroft School project

Future Projected State Funding: \$9.5M

TOTAL PROJECT BUDGET: \$82M



PROJECT BUDGET \$82M

PROJECT SCHEMATIC DESIGN ESTIMATE:

BUILDING \$ 78.5M SITE WORK & DEMOLITION \$ 10.2M

ESTIMATE TOTAL \$88.7M*

*Estimate Value INCLUDES \$4.6M in Project Contingency

Current Budget Gap: \$6.7M

POTENTIAL DESIGN ALTERNATES FOR COST REDUCTION ONGOING



POTENTIAL ALTERNATES / CONSIDERATIONS TO MEET BUDGET CONSTRAINTS

Alternates/Scope Reduction Items

Delete (4) Classrooms / (2) Commons

Delete 5th Grade Learning Commons

Addl. Misc. VE (Bldg. systems/materials)

Reduce Curtainwall (Full ht. glass)

Reduce Auditorium Systems

Shell Library / Auditorium / Music

Delete Bleachers @ Gym





Next Steps



- Programming/Ed Spec Phase Complete (May 12, 2021)
- Schematic Design Phase (September 2021)
- Design Development Phases (Late Fall 2021)
- Relocation of Drew (Early 2022)
- Construction Contract Bid Approval(s)

(Various: Late 2021-Early 2022)

<u>Note</u>: All dates will be coordinated with Construction Manager's master schedule.





Questions & Answers







Presentation to Board of Education

December 7, 2021
